

TRADE SECRET



July 20, 2009

Mr. Reece McAlister
Executive Secretary
Georgia Public Service Commission
244 Washington Street, First Floor
Atlanta, Georgia 30334-5701

RE: Georgia Power's June 2009 Monthly Status Report; Docket No. 29849-U

Dear Mr. McAlister:

On March 30, 2009, the Georgia Public Service Commission (the "Commission") issued Its Amended Certification Order approving the certification of Plant Vogtle Units 3 and 4 in the above styled docket. As part of that Order the Commission adopted a stipulation (the "Stipulation") between the Public Interest Advocacy Staff (the "PIA Staff") and Georgia Power Company (the "Company"). The Stipulation provides for the filing of monthly status reports with the Commission on the construction work in progress. Estimates of costs and schedules contained in this Report are based upon best information available. The schedule and budget for Vogtle Units 3 and 4 are subject to change and may be revised as conditions necessitate.

This filing contains certain information that is being filed under the Commission's trade secret rules. Therefore, five (5) copies of a redacted version of such information and the basis for the trade secret assertion are enclosed for public disclosure.

Should you have any questions, please call me at 404-506-6245 or Dick White at 404-506-2393.

Sincerely,

Jim R. Fletcher

Jim R. Fletcher
Manager, Regulatory Affairs

(JW)

Enclosures

c: Sheree Kernizan, Georgia Public Service Commission
Daniel Cearfoss, Georgia Public Service Commission

**Basis for the Assertion that Redacted Portions of Georgia Power Company's
Plant Vogtle Units 3 and 4 Construction Monitoring Status Report
are Protected Trade Secrets**

As part of construction monitoring process following the certification of Units 3 and 4 at Plant Vogtle, Georgia Power Company ("Georgia Power" or "the Company") submits to the Georgia Public Service Commission (the "Commission"): (1) an Executive Summary; (2) Georgia Power's Project Cost Detail and Budget Update; (3) Critical Path Schedule; (4) Status of NRC Licensing; and (5) Status of licenses and permits (the "Report"). Certain provisions of the Report are trade secrets of Georgia Power, Southern Company, Oglethorpe Power Corporation, Municipal Electric Authority of Georgia, and the City of Dalton (collectively the "Co-owners"), Westinghouse Electric Company LLC ("Westinghouse"), and Stone & Webster, Inc., and their affiliates and are protected under Commission Rule 515-3-1-.11.

The trade secret provisions of the Report derive economic value from not being generally known to, and not being readily ascertainable by proper means by other persons who can obtain economic value from their disclosure or use. Public disclosure of the trade secret information in the Report could give competitors of Westinghouse an unfair advantage by showing the Company's costs and project configuration. Disclosure of this information could also interfere with the Company's ability to negotiate for best cost equipment from vendors. Disclosure could also severely harm Westinghouse and Stone & Webster, Inc. and that harm could in turn impair Georgia Power, the Co-owners and their customers. Additionally, the trade secret portions of the Report are subject to extensive efforts to maintain their secrecy.

Only select Georgia Power and Southern Company personnel and their legal counsel are granted access to the trade secret portions of the Report. Those personnel receive access only on a "need to know" basis. If a party outside Georgia Power and Southern Company and their legal counsel are granted access to the trade secret portions of the Report, the party is required to sign a confidentiality agreement with respect to the trade secret portions of the Report.

More specifically, the information that has been redacted pertaining to the proposed nuclear units contains pricing, scheduling, and sensitive invoicing information that is specific to Vogtle Units 3 and 4. This information is considered confidential and proprietary by the Company and its contractors and not generally known by the public. Revealing these terms would compromise the Company's ability to procure the best cost resources from equipment suppliers or independent power suppliers in future solicitations. In the event such information were released, it is quite likely that suppliers for future generating equipment purchases would use this information to set the floor on negotiated pricing or that bidders in future Request For Proposals would use this information to set the floor in constructing their own bids, thus artificially and inefficiently setting a market price and other generation characteristics for the Company that may not be representative of the best cost or best resource that the market could

offer. Furthermore, the parties to current equipment negotiations have agreed to maintain the confidentiality of these terms.

Amongst the items that are redacted are highly sensitive terms, pricing, and indexing originally found in the Engineering, Procurement, Construction Agreement ("EPC Agreement") that the Company entered last year with Westinghouse and Stone & Webster, Inc. for the development of Vogtle Units 3 and 4. The costing, terms and indexing methodology employed in the EPC Agreement are proprietary information that, if publicly available, could be used by Westinghouse's competitors to tailor offerings to other utilities and place Westinghouse at a competitive disadvantage because Westinghouse would not have access to comparable information regarding its competitors' terms, pricing and indexing.

Moreover, public release of the confidential information included in the Report could have adverse economic consequences for the Company. Public release of the confidential information could make potential vendors unwilling or unable to conduct business with the Company. By causing the vendors' proprietary information to be publicly available, even fewer vendors might be willing to sell to the Company, thus, reducing the opportunity for the Company to purchase the equipment best suited to meeting its customers' needs and potentially compelling the Company to deal with a vendor that does not offer the best cost option. This could cause significant added costs to the Company and ultimately to Georgia Power's ratepayers. Additionally, public release of the EPC Agreement information in the Report would provide competitors of Georgia Power with unfair access to information regarding the Company's costs. Information regarding the costs included in the EPC Agreement could be used to assess the costs of energy bid into the wholesale market by Georgia Power. This information could allow the Company's competitors to tailor their wholesale energy bids to undermine the Company's competitive position and consequently to adversely impact the Company's revenues and profits.

Vogle Monthly Status Report Through June 30, 2009

Table of Contents

Executive Summary	1
Project Cost to Date Update	2
Year to Date Budget Update	3
Unit 3 Critical Path Schedule	4
Unit 4 Critical Path Schedule	5
Early Site Permit (ESP) Review Schedule	6
Construction & Operating License Application (COLA) Review Schedule	7
Permits Update	8

PUBLIC DISCLOSURE

Executive Summary Vogtle Monthly Status Report Through June 30, 2009

Capital Expenditures (in millions of \$) Georgia Power Ownership

Actual Expenditures through June 2009

Direct	\$ REDACTED
AFUDC	\$ REDACTED
Total for Project	\$ REDACTED

Project budget as of June 2009

Total Project Cost Forecast	\$ REDACTED
Total Certification Amount	\$ REDACTED

CHART

REDACTED

Major Milestones Achieved

- June 22, 2009: Atomic Safety and Licensing Board (ASLB) ruled in SNC's favor on all contested issues in the ESP hearing. NRC is scheduled to issue a ruling on the uncontested issues in August 2009.
- REDACTED
- REDACTED

Overall Project Status

- REDACTED

Notes

- REDACTED
- REDACTED

PUBLIC DISCLOSURE
Vogle 3 & 4 Project
Georgia Power Company Cost
Project Cost To-Date
June 2009

(Millions of \$)	Total Certification Cost	Total Current Forecast	Actual to Date	Budget to Date	Variance	Notes on Variance
Capital						
EPC	\$ REDACTED	\$ REDACTED	\$ REDACTED	\$ REDACTED	\$ REDACTED	REDACTED
Owners' Cost	\$ REDACTED	\$ REDACTED	\$ REDACTED	\$ REDACTED	\$ REDACTED	REDACTED
AFUDC	\$ REDACTED	\$ REDACTED	\$ REDACTED	\$ REDACTED	\$ REDACTED	REDACTED
Ad Valorem	\$ REDACTED	\$ REDACTED	\$ REDACTED	\$ REDACTED	\$ REDACTED	REDACTED
Test Fuel Offsets	\$ REDACTED	\$ REDACTED	\$ REDACTED	\$ REDACTED	\$ REDACTED	REDACTED
Transmission Interconnection	\$ REDACTED	\$ REDACTED	\$ REDACTED	\$ REDACTED	\$ REDACTED	REDACTED
Total Capital	\$ REDACTED	\$ REDACTED	\$ REDACTED	\$ REDACTED	\$ REDACTED	REDACTED

Area	Variance Explanation
EPC (1)	REDACTED
Owners' Cost (2)	REDACTED
AFUDC	REDACTED
Ad Valorem	REDACTED
Test Fuel Offsets	REDACTED
Transmission Interconnection	REDACTED

PUBLIC DISCLOSURE
Vogtle 3 & 4 Project
Georgia Power Company Cost
Year-to-Date Budget Update
June 2009

(Millions of \$)	YTD Actual	YTD Budget	YTD Variance	Notes on Variance
Capital				
EPC	\$ REDACTED	\$ REDACTED	\$ REDACTED	REDACTED
Owners' Cost	\$ REDACTED	\$ REDACTED	\$ REDACTED	REDACTED
AFUDC	\$ REDACTED	\$ REDACTED	\$ REDACTED	REDACTED
Ad Valorem	\$ REDACTED	\$ REDACTED	\$ REDACTED	REDACTED
Test Fuel Offsets	\$ REDACTED	\$ REDACTED	\$ REDACTED	REDACTED
Transmission Interconnection	\$ REDACTED	\$ REDACTED	\$ REDACTED	REDACTED
Total Capital	\$REDACTED	\$REDACTED	\$REDACTED	REDACTED


Area	Variance Explanation
EPC (1)	REDACTED
Owners' Cost (2)	REDACTED
AFUDC	REDACTED
Ad Valorem	REDACTED
Test Fuel Offsets	REDACTED
Transmission Interconnection	REDACTED

LEVEL ONE CRITICAL PATH

VOGTLE UNIT 3

July 2009

DATA DATE 6-26-2009

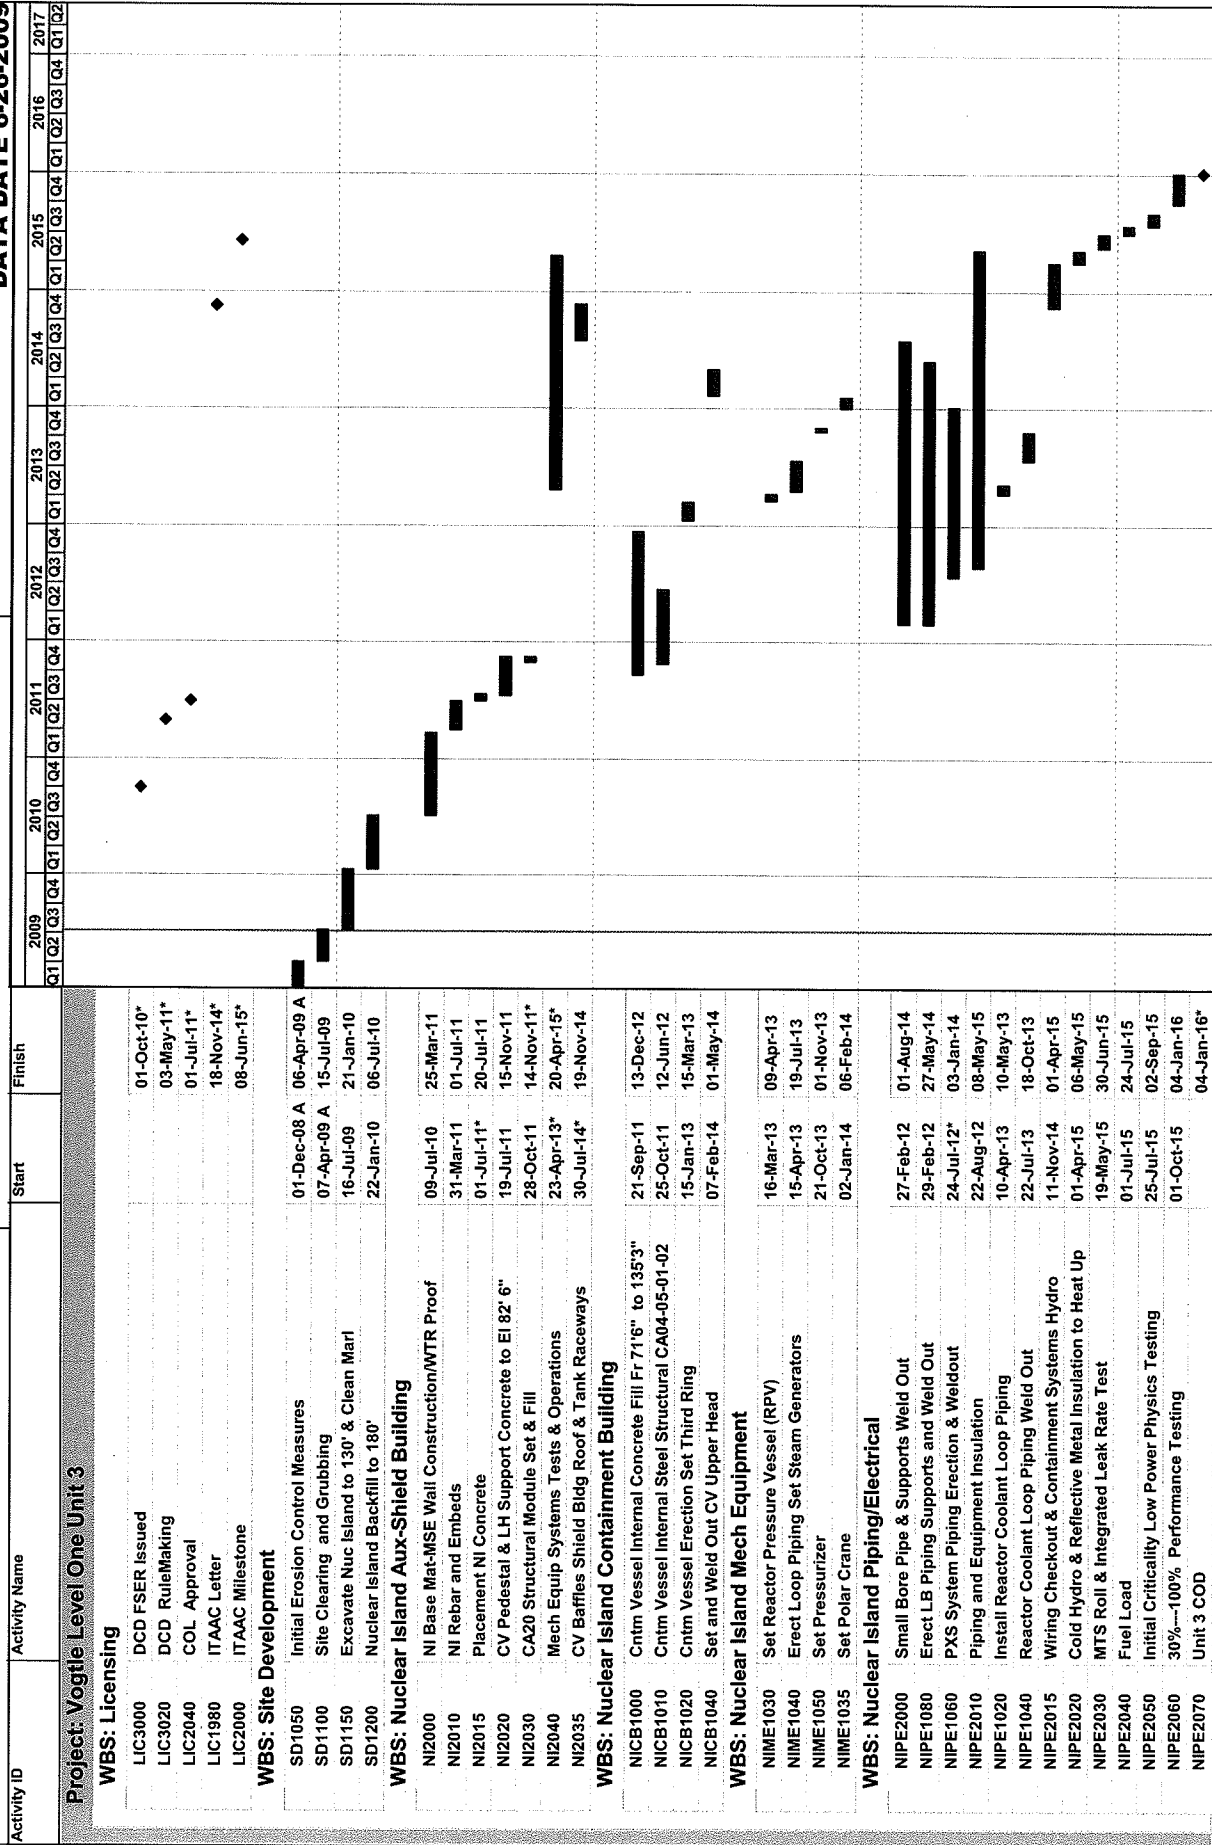

Page 1 of 1

Actual Work Remaining Work
Remaining Work Milestone

* = Constraint Dates

LEVEL ONE CRITICAL PATH

VOGTLE UNIT 4

July 2009

DATA DATE 6-26-2009

Activity ID	Activity Name	Start	Finish	2009	2010	2011	2012	2013	2014	2015	2016	2017
				Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
Project: Vogtle Level One Unit 4												
WBS: Nuclear Island Aux-Shield Building												
NISB2000	NI Base Mat-MSE Wall Construction/WTR Proof	28-Jul-10*	18-Apr-11									
NISB2010	NI Rebar and Embeds	30-Apr-12	02-Jul-12									
NISB2015	Placement NI Concrete	02-Jul-12	19-Jul-12									
NISB2020	CV Pedestal & LH Support Concrete to El 82' 6"	17-Jul-12	14-Nov-12									
NISB2030	CA20 Structural Module Set & Fill	20-Sep-12	05-Oct-12									
NISB2040	Mech Equip Systems Tests & Operations	13-Feb-14*	21-Apr-16									
NISB2060	Instrumentation and Controls Installation	26-Jun-14*	18-Aug-14									
NISB2050	Power and Control Cable Installation	18-Aug-14*	27-Jul-15									
NISB2070	Aux Building System Hydro	20-Nov-14*	02-Nov-15									
NISB2035	CV Baffles Shield Bldg Roof & Tank	01-Jul-15*	23-Nov-15									
WBS: Nuclear Island Containment Building												
NICB1010	Cntm Vessel Internal Steel Structural CA04-05-01-02	02-Aug-12	14-Jun-13									
NICB1000	Cntm Vessel Internal Concrete Fill Fr 71'6" to 135'3"	20-Sep-12*	17-Dec-13									
NICB1020	Cntm Vessel Erection Set First Ring & Weld Out	04-Jan-13*	26-Mar-13									
NICB1030	Cntm Vessel Erection Set Second Ring & Weld Out	05-Aug-13	04-Oct-13									
NICB1040	Cntm Vessel Erection Set Third Ring & Weld Out	20-Jan-14	19-Mar-14									
NICB1050	Set and Weld Out CV Upper Head	11-Feb-15*	04-May-15									
WBS: Nuclear Island Mech Equipment												
NIME1030	Set Reactor Pressure Vessel (RPV)	20-Mar-14	11-Apr-14									
NIME1040	Erect Loop Piping Set Steam Generators	15-Apr-14	23-Jul-14									
NIME1050	Set Pressurizer	22-Oct-14	05-Nov-14									
NIME1055	Set Polar Crane	06-Jan-15*	10-Feb-15									
WBS: Nuclear Island Piping/Electrical												
NIPE2000	Small Bore Pipe & Supports Weld Out	26-Feb-13*	04-Aug-15									
NIPE1080	Erect LB Piping Supports and Weld Out	27-Feb-13*	29-May-15									
NIPE1060	PXS System Piping Erection & Weldout	26-Jul-13*	07-Jan-15									
NIPE2010	Piping and Equipment Insulation	26-Aug-13*	11-May-16									
NIPE1020	Install Reactor Coolant Loop Piping	11-Apr-14	14-May-14									
NIPE1040	Reactor Coolant Loop Piping Weld Out	23-Jul-14	22-Oct-14									
NIPE2015	Wiring Checkout & Containment Systems Hydro	12-Nov-15*	01-Apr-16									
WBS: Main Containment System Startup												
MCS2050	RCS Reactor Coolant System Operations Testing	13-Jan-15*	25-Mar-16									
MCS2040	PXS Passive Core Cooling System Operations Testing	30-Mar-15*	29-Jan-16									
MCS2030	CVS Chemical & Volume Control System Operations Testing	14-Dec-15*	02-May-16									
MCS2070	Cold Hydro & Reflective Metal Insulation	28-Mar-16	06-May-16									
MCS2080	MTS Roll & Integrated Leak Rate Test	19-May-16	29-Jun-16									
MCS2090	Fuel Load	01-Jul-16	26-Jul-16									
MCS2100	Initial Criticality Low Power Physics Testing	26-Jul-16	06-Sep-16									
MCS2110	30-100% Performance Testing	03-Oct-16	03-Jan-17									
MCS2120	Unit # 4 COD Commercial Operations Date		03-Jan-17*									

Page 1 of 1

Actual Work Remaining Work Critical Remaining Work
 Remaining Work ◆ Milestone

* = Constraint Dates

Licensing - ESP Review Schedule

(Future Activities from NRC's June 26 Letter and ASLB July 3 Order)

Description	Current Date
NRC issues seismic RAIs	Jul 21, 2008 (A)
SNC responds to RAIs	Aug 14, 2008(A)
NRC issues Final Environmental Impact Statement	Aug 14, 2008(A)
NRC collects seismic SER input from reviewers	Oct 20, 2008 (A)
NRC issues Advanced Final Safety Evaluation Report for ACRS	Nov 12, 2008(A)
ACRS Sub/Full Committee Meeting on ESPA	Dec 3/4, 2008(A)
NRC issues Final Safety Evaluation Report as NUREG	Feb 5, 2009 (A)
ASLB Limited Appearance Sessions for Mandatory Hearing, Motions, Testimony, Mandatory and Intervention Contention Hearings	March 2009 (A)
ASLB Decision on Intervention Contentions	June 22, 2009(A)
ASLB Decision on Mandatory Hearing	August 17, 2009
ESP Issued (Based on August 7, 2007 Part 2 changes)	August 27, 2009

(A) - Actual

Blue dates are from the NRC. Black represents a projection based on typical schedule.

Plant Vogtle Units 3 & 4

Licensing - Vogtle 3 & 4 COLA Schedule

(Future Activities from NRC telecon of June 22 in Blue)

Description	Date
SNC starts Application development	Jun 01, 2006 (A)
SNC submits Application	Mar 31, 2008 (A)
NRC completes sufficiency review	May 30, 2008 (A)
Requests for information with the Staff	Jul 2008 – Jan 14, 2009 (A)
NRC conducts public meeting of overall submittal	Jul 17, 2008 (A)
NRC notices availability and opportunity for intervention	Sep 16, 2008 (A)
NRC issues draft environmental impact statement	Apr 17, 2009 (delayed)
NRC conducts public environmental meeting	May 2009 (delayed)*
NRC issues BLN SER with open items	Feb 2010
ACRS conducts review on SER material	July 2009 – April 2010
NRC issues final environmental impact statement	Jan 15, 2010 (delayed)
NRC issues final SER with no open items for ACRS (45 day float)	Oct 25, 2010
ACRS conducts review on final SER (5 day float)	Feb 16, 2011
NRC issues NUREG final SER (10 days float)	Apr 12, 2011
NRC conducts ASLB activities	Jul 2010 – Sep 2011*
NRC issues COL for Vogtle 3 and 4	Oct 2011**

* Schedules based on the durations of the published Part 2.

** Based on EPC Contractual Commercial Operation Date of 4/16/2016, not the Target Schedule Date of 1/4/2016 for Unit 3

(A) - Actual

Plant Vogtle Units 3 & 4

PUBLIC DISCLOSURE

Plant Vogtle Units 3 and 4 Environmental Permits & Plans

Anticipated Commercial Operation Date: April 2016

Permit	Activity Covered	Permitting Agency	Jurisdiction	Estimated Application Date	Projected Received Date	Required Date	Responsibility	Notes
Early Site Permit (ESP) and Limited Work Authorization (LWA)	ESP -Site approval for nuclear plant construction; LWA - approval for limited safety-related work	NRC	Federal	Actual August 2006	REDACTED	REDACTED	SNC	
	Safety related construction for a nuclear power facility	NRC	Federal	Actual March 31, 2008	REDACTED	REDACTED	SNC	
Section 404 Permit	Disturbance of crossing wetland areas or navigable waters	USACE	Federal	REDACTED	REDACTED	REDACTED	SNC	1, 7,8
Section 10 Permit	Barge slip, new intake/discharge to Savannah River	USACE	Federal	REDACTED	REDACTED	REDACTED	SNC	1, 7,8
Section 401 Certification	Compliance with water quality standards	GDNR	State	REDACTED	REDACTED	REDACTED	SNC	7.8
State Waters Buffer Variance	Land disturbing activities within 25' state waters buffer	GDNR	State	REDACTED	REDACTED	REDACTED	SNC	
	Transportation of Hazardous Material	USDOT	Federal	Actual May 14, 2009	Actual May 14, 2009	REDACTED	SNC	11
Federal Depredation Permit	Adverse impacts on protected species and/or their nests. For site and rail corridor upgrade.	USFWS	Federal	If needed	TBD	TBD	SNC/GPC	
Scientific Collecting Permit	Collection of specimens	USFWS	Federal	If needed	TBD	TBD	SNC/GPC	

PUBLIC DISCLOSURE

Anticipated Commercial Operation Date: April 2016

Plant Vogtle Units 3 and 4 Environmental Permits & Plans

Permit	Activity Covered	Permitting Agency	Jurisdiction	Estimated Application Date	Projected Received Date	Required Date	Responsibility	Notes
Salvage Permit	Donation or receipt of protected species (bodies, feathers, etc.) for exhibit or scientific study	USFWS	Federal	If needed	TBD	TBD	SNC/GPC	
Objects Affecting Navigable Airspace - Construction Notice	Notice of erection of structures (>200' high) potentially impacting air navigation	FAA	Federal	REDACTED	REDACTED	REDACTED	Shaw	
Stand-Alone Construction Projects Storm Water Permit	Discharge storm water from site during construction	GDNR	State	Actual October 2008	Ongoing	Various	SNC	
National Historic Preservation Act	Consultation regarding potential to adversely affect historic resources	GDNR	State	REDACTED	REDACTED	REDACTED	SNC	7, 9
Air Quality Construction Permit	Construction air emission sources	GDNR	State	Actual March 13, 2009	REDACTED	REDACTED	Shaw	10
NPDES Wastewater Permit	Regulates limits of pollutants in liquid discharge to surface water	GDNR	State	REDACTED	REDACTED	REDACTED	SNC	2,7
Air Quality Construction Permit	Construction of plant air emission sources	GDNR	State	Actual May 22, 2009	REDACTED	REDACTED	SNC	
GA Endangered Wildlife Act	Adverse impacts on state designated protected species and/or their habitat. For site and rail corridor	GDNR	State	If needed	TBD	TBD	SNC	

PUBLIC DISCLOSURE

Plant Vogtle Units 3 and 4 Environmental Permits & Plans

Anticipated Commercial Operation Date: April 2016

Permit	Activity Covered	Permitting Agency	Jurisdiction	Estimated Application Date	Projected Received Date	Required Date	Responsibility	Notes
NPDES Wastewater Permit	Regulates limits of pollutants in liquid discharge to surface water	GDNR	State	TBD	TBD	REDACTED	SNC	3
NPDES Wastewater Permit	Regulates limits of pollutants in liquid discharge to surface water	GDNR	State	TBD	TBD	REDACTED	SNC	3
Infrastructure Projects Construction Storm Water Permit	Discharge storm water from linear construction sites (e.g. Roadways, transmission line and rail corridor)	GDNR	State	TBD	TBD	REDACTED	GPC	
General Permit for Industrial Storm Water Discharges	Discharge storm water associated with industrial activity	GDNR	State	TBD	TBD	REDACTED	SNC	4
Permit to Operate a Public Water System	Operate a public, non-transient, non-community water system	GDNR	State	Actual June 16, 2009	REDACTED	REDACTED	SNC	4
Permit to Withdraw Groundwater – Make up Wells 3 and 4	Consumptive use of 100,000 gallons per day or more of groundwater	GDNR	State	Actual May 26, 2009	REDACTED	REDACTED	SNC	4
Permit to Withdraw Groundwater – Dewatering Activities	Dewater for foundation if needed for more than 60 days	GDNR	State	Actual September 3, 2008	Actual March 27, 2009	REDACTED	SNC	
Certificate of Abandoned Well(s) – MU-2A	Abandoned wells have been filled, plugged and sealed (notification required 30 days after well is abandoned)	GDNR	State	REDACTED	N/A No response required	REDACTED	SNC	

PUBLIC DISCLOSURE

Plant Vogtle Units 3 and 4 Environmental Permits & Plans

Anticipated Commercial Operation Date: April 2016

Permit	Activity Covered	Permitting Agency	Jurisdiction	Estimated Application Date	Projected Received Date	Required Date	Responsibility	Notes
Certificate of Abandoned Well(s) – SW-5	Abandoned wells have been filled, plugged and sealed (notification required 30 days after well is abandoned)	GDNR	State	Actual February 18, 2009 Notification only	NA – No response required	NA	SNC	
Permit to Withdraw Surface Water	Surface water withdrawal	GDNR	State	REDACTED	REDACTED	REDACTED	SNC	4
Land Disturbing Activity Permit	Permission to conduct land disturbing activities of one acre or larger, or within 25' of any state waters	GDNR	State	N/A	N/A	N/A		5
Private Industrial Landfill Permit	On-site disposal of solid waste consisting of construction and demolition debris	GDNR	State	REDACTED	Actual Revised D & O Plan Received April 30, 2009	REDACTED	SNC	4
Solid Waste Handling Permit	Disposal of industrial solid wastes; transportation of putrescible waste for disposal in a permitted landfill	GDNR	State	N/A	N/A	N/A	SNC	6
Title V Operating Permit	Operation of air emission sources	GDNR	State	TBD	REDACTED	REDACTED	SNC	4
Certificate of Public Convenience and Necessity	Present and future public convenience and necessity requiring the operation of such equipment or facility	GA PSC	State	Actual August 1, 2008	Actual March 17, 2009 Approved by PSC	REDACTED	GPC	

PUBLIC DISCLOSURE

Plant Vogtle Units 3 and 4 Environmental Permits & Plans

Anticipated Commercial Operation Date: April 2016

Permit	Activity Covered	Permitting Agency	Jurisdiction	Estimated Application Date	Projected Received Date	Required Date	Responsibility	Notes
General Permit to Transport Radioactive Materials	Transportation of radioactive materials in the State of Georgia	GDNRR/ GDPS	State	TBD	REDACTED	REDACTED	SNC	4
Utility Right-of-Way Permit	Utility right-of-way easement	GDOT	State	TBD	REDACTED	REDACTED	GPC	
Tennessee Radioactive Waste License-for-Delivery	Transportation of radioactive materials into the State of Tennessee	TDEC	State	TBD	REDACTED	REDACTED	SNC	4
Utah Radiation Control Rule	Transportation of radioactive materials into the State of Utah	UDEQ	State	TBD	REDACTED	REDACTED	SNC	4
Scientific Collecting Permit	State permit for collection of specimens	SCDNR	State	If needed	TBD	TBD	SNC/GPC	
Scientific Collecting Permit	State permit for collection of specimens	GDNRR	State	If needed	TBD	TBD	SNC/GPC	
Land Disturbing Activity Permit	All land disturbing activities within the boundaries of Burke County	Burke County	County	N/A	N/A	N/A	N/A	5
Building Permit	Construction, alteration, repair, or demolition of any building or structure within the boundaries of Burke County	Burke County	County	N/A	N/A	N/A	N/A	5
Demolition Notification	Notice of demolition of buildings or structures	GDNRR/ Burke County	State/ County	Various – first notification submitted in October 2008	Various	Various	SNC	

PUBLIC DISCLOSURE

Plant Vogtle Units 3 and 4 Environmental Permits & Plans

Anticipated Commercial Operation Date: April 2016

Permit	Activity Covered	Permitting Agency	Jurisdiction	Estimated Application Date	Projected Received Date	Required Date	Responsibility	Notes
Land Disturbing Activity Permit	All land disturbing activities within the boundaries for transmission construction	Various	County	N/A	N/A	N/A	N/A	5

Notes on Variances

1	Permit application to be submitted in accordance with USACE regulations; Corps Master permit to cover barge slip, intake and discharge.							
2	If needed for Batch Plant							
3	Modification to existing permit – one for Unit 3 and one for Unit 4							
4	Modification to existing permit; early filing planned pending receipt of intake design from Shaw							
5	Not applicable since GPC is exempt pursuant to O.C.G.A 12-7-17 (10)							
6	Existing Permit – no modification required							
7	Pending final design info from Shaw							
8	All items related to Corps Master permit							
9	MOU for SHPO temporarily delayed pending evaluation of Shaw inquiry on potential for relocation of intake structure							
10	Shaw Air SIP permit for construction issued June 18, 2009 by Georgia EPD; modification of permit will be required due to changes in equipment needs and specifications by Shaw. Permit modification in process.							
11	Electronic renewal process							
